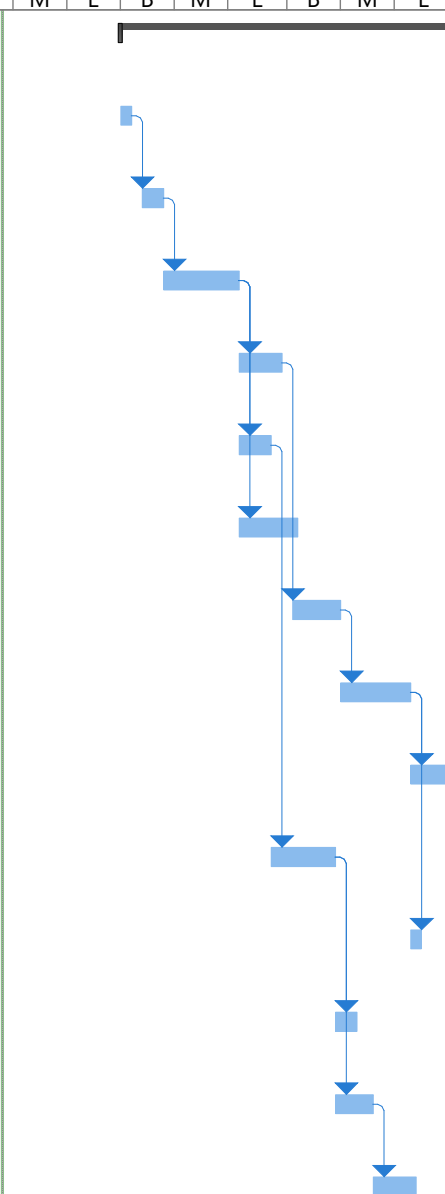


ID	Task Name	Duration	Start	Finish	November			December			January			Febr
					B	M	E	B	M	E	B	M	E	B
1	Reliable Construction Co. Project	43 days	Thu 12/1/16	Mon 1/30/17										
2	A Excavate	2 days	Thu 12/1/16	Fri 12/2/16										
3	B Foundation	4 days	Mon 12/5/16	Thu 12/8/16										
4	C Rough Wall	10 days	Fri 12/9/16	Thu 12/22/16										
5	D Roof	6 days	Fri 12/23/16	Fri 12/30/16										
6	E Exterior Plumbing	4 days	Fri 12/23/16	Wed 12/28/16										
7	I Electrical Work	7 days	Fri 12/23/16	Mon 1/2/17										
8	G Exterior Sliding	7 days	Mon 1/2/17	Tue 1/10/17										
9	H Exterior Painting	9 days	Wed 1/11/17	Mon 1/23/17										
10	F Interior Plumbing	5 days	Tue 1/24/17	Mon 1/30/17										
11	J Wallboard	8 days	Thu 12/29/16	Mon 1/9/17										
12	M Exterior Fixtures	2 days	Tue 1/24/17	Wed 1/25/17										
13	K Flooring	4 days	Tue 1/10/17	Fri 1/13/17										
14	L Interior Painting	5 days	Tue 1/10/17	Mon 1/16/17										
15	N Interior Fixtures	6 days	Tue 1/17/17	Tue 1/24/17										

Start No Earlier Than
